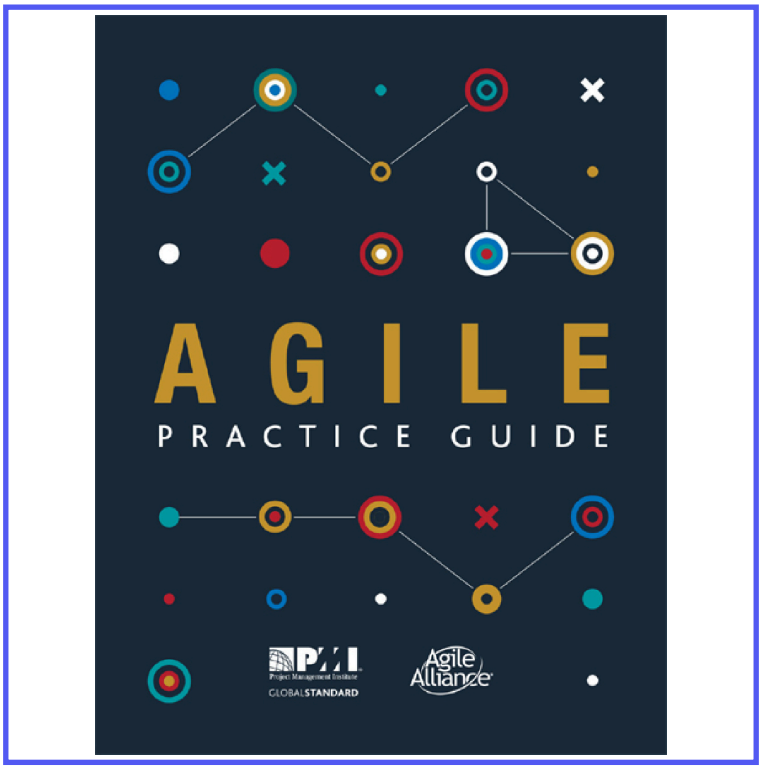


ebookbig.com

or scan the QR code to access the digital study portal.

NOTICE

The Project Management Institute, Inc. (PMI) standards and guideline publications, of which the document contained herein is one, are developed through a voluntary consensus standards development process. This process brings together volunteers and/or seeks out the views of persons who have an interest in the topic covered by this publication. While PMI administers the process and establishes rules to promote fairness in the development of consensus, it does not write the document and it does not independently test, evaluate, or verify the accuracy or completeness of any information or the soundness of any judgments contained in its standards and guideline publications.

PMI disclaims liability for any personal injury, property or other damages of any nature whatsoever, whether special, indirect, consequential or compensatory, directly or indirectly resulting from the publication, use of application, or reliance on this document. PMI disclaims and makes no guaranty or warranty, expressed or implied, as to the accuracy or completeness of any information published herein, and disclaims and makes no warranty that the information in this document will fulfill any of your particular purposes or needs. PMI does not undertake to guarantee the performance of any individual manufacturer or seller's products or services by virtue of this standard or guide.

In publishing and making this document available, PMI is not undertaking to render professional or other services for or on behalf of any person or entity, nor is PMI undertaking to perform any duty owed by any person or entity to someone else. Anyone using this document should rely

on his or her own independent judgment or, as appropriate, seek the advice of a competent professional in determining the exercise of reasonable care in any given circumstances. Information and other standards on the topic covered by this publication may be available from other sources, which the user may wish to consult for additional views or information not covered by this publication.

PMI has no power, nor does it undertake to police or enforce compliance with the contents of this document. PMI does not certify, test, or inspect products, designs, or installations for safety or health purposes. Any certification or other statement of compliance with any health or safety-related information in this document shall not be attributable to PMI and is solely the responsibility of the certifier or maker of the statement.

PREFACE

The Project Management Institute and Agile Alliance® chartered this practice guide to create a greater understanding of agile approaches in their communities. The vision for this practice guide is to equip project teams with tools, situational guidelines, and an understanding of the available agile techniques and approaches to enable better results.

Project teams are using agile approaches in a variety of industries beyond software development. Both organizations realize that expansion has created a need for a common language, open mindedness, and the willingness to be flexible in how products and deliverables are brought to market. In addition, both organizations realize there are multiple ways to achieve successful delivery. There are a broad range of tools, techniques, and frameworks; teams have choices for approaches and practices that fit their project and the organizational culture in order to achieve the desired outcome.

The *Agile Practice Guide* core committee members are from varying backgrounds and use various approaches. Some of the committee members are consultants and some work inside organizations. All have worked in agile ways for many years.

TABLE OF CONTENTS

1. INTRODUCTION

2. AN INTRODUCTION TO AGILE
    - 2.1 Definable Work vs. High-Uncertainty Work
    - 2.2 The Agile Manifesto and Mindset
    - 2.3 Lean and the Kanban Method
    - 2.4 Uncertainty, Risk, and Life Cycle Selection

3. LIFE CYCLE SELECTION
    - 3.1 Characteristics of Project Life Cycles
        - 3.1.1 Characteristics of Predictive Life Cycles
        - 3.1.2 Characteristics of Iterative Life Cycles
        - 3.1.3 Characteristics of Incremental Life Cycles
        - 3.1.4 Characteristics of Agile Life Cycles
        - 3.1.5 Agile Suitability Filters
        - 3.1.6 Characteristics of Hybrid Life Cycles
        - 3.1.7 Combined Agile and Predictive Approaches
        - 3.1.8 Predominantly Predictive Approach with Some Agile Components
        - 3.1.9 A Largely Agile Approach with a Predictive Component
        - 3.1.10 Hybrid Life Cycles as Fit-For-Purpose

3.1.11 Hybrid Life Cycles as Transition Strategy
3.2 Mixing Agile Approaches
3.3 Project Factors That Influence Tailoring
4. IMPLEMENTING AGILE: CREATING AN AGILE ENVIRONMENT
4.1 Start with an Agile Mindset
4.2 Servant Leadership Empowers the Team
4.2.1 Servant Leader Responsibilities
4.2.2 Role of the Project Manager in an Agile Environment
4.2.3 Project Managers Use Servant Leadership
4.3 Team Composition
4.3.1 Agile Teams
4.3.2 Agile Roles
4.3.3 Generalizing Specialists
4.3.4 Team Structures
4.3.5 Dedicated Team Members
4.3.6 Team Workspaces
4.3.7 Overcoming Organizational Silos
5. IMPLEMENTING AGILE: DELIVERING IN AN AGILE ENVIRONMENT
5.1 Charter the Project and the Team
5.2 Common Agile Practices
5.2.1 Retrospectives
5.2.2 Backlog Preparation
5.2.3 Backlog Refinement
5.2.4 Daily Standups
5.2.5 Demonstrations/Reviews
5.2.6 Planning for Iteration-Based Agile
5.2.7 Execution Practices that Help Teams Deliver Value

5.2.8 How Iterations and Increments Help Deliver Working Product
5.3 Troubleshooting Agile Project Challenges
5.4 Measurements in Agile Projects
5.4.1 Agile Teams Measure Results

6. ORGANIZATIONAL CONSIDERATIONS FOR PROJECT AGILITY
6.1 Organizational Change Management
6.1.1 Drivers for Change Management
6.1.2 Readiness for Change
6.2 Organizational Culture
6.2.1 Creating an Environment of Safety
6.2.2 Assessing Culture
6.3 Procurement and Contracts
6.4 Business Practices
6.5 Multiteam Coordination and Dependencies (Scaling)
6.5.1 Frameworks
6.5.2 Considerations
6.6 Agile and the Project Management Office (PMO)
6.6.1 An Agile PMO is Value-Driven
6.6.2 An Agile PMO is Invitation-Oriented
6.6.3 An Agile PMO is Multidisciplinary
6.7 Organizational Structure
6.8 Evolving the Organization

7. A CALL TO ACTION

ANNEX A1
PMBOK® GUIDE MAPPING

ANNEX A2
AGILE MANIFESTO MAPPING

ANNEX A3
OVERVIEW OF AGILE AND LEAN FRAMEWORKS

APPENDIX X1
CONTRIBUTORS AND REVIEWERS

APPENDIX X2
ATTRIBUTES THAT INFLUENCE TAILORING

APPENDIX X3
AGILE SUITABILITY FILTER TOOLS

REFERENCES

BIBLIOGRAPHY

GLOSSARY

LIST OF TABLES AND FIGURES

Figure 2-1. The Four Values of the Agile Manifesto

Figure 2-2. The Twelve Principles Behind the Agile Manifesto

Figure 2-3. The Relationship Between the Agile Manifesto Values, Principles, and Common Practices

Figure 2-4. Agile is a Blanket Term for Many Approaches

Figure 2-5. Uncertainty and Complexity Model Inspired by the Stacey Complexity Model

Figure 3-1. The Continuum of Life Cycles

Figure 3-2. Predictive Life Cycle

Figure 3-3. Iterative Life Cycle

Figure 3-4. A Life Cycle of Varying-Sized Increments

Figure 3-5. Iteration-Based and Flow-Based Agile Life Cycles

Figure 3-6. Agile Development Followed by a Predictive Rollout

Figure 3-7. A Combined Agile and Predictive Approach Used Simultaneously

Figure 3-8. A Largely Predictive Approach with Agile Components
Figure 3-9. A Largely Agile Approach with a Predictive Component
Figure 5-1. Burndown Chart for Remaining Story Points
Figure 5-2. Burnup Chart for Showing Story Points Completed
Figure 5-3. Example of a Kanban Board
Figure 5-4. Feature Chart
Figure 5-5. Product Backlog Burnup Chart
Figure 5-6. Earned Value in an Agile Context
Figure 5-7. Cumulative Flow Diagram of Completed Features
Figure 6-1. The Relationship Between Change Management and Agile Approaches
Figure 6-2. Example of Assessing Organizational Culture
Figure 6-3. Initial Ranked Backlog for Changes
Figure 6-4. Using Backlogs and Kanban Boards to Organize and Track Change Work
Figure A3-1. Agile Approaches Plotted by Breadth and Detail
Figure A3-2. Kanban Board Demonstrating Work in Progress Limits, and a Pull System to Optimize the Flow of Work
Figure A3-3. The Crystal Family of Methods
Figure A3-4. Feature-Driven Development Project Life Cycle
Figure A3-5. DSDM Approach to Constraint-Driven Agility
